

PREPARED FOR



DELIVERED BY



— ODS ASSESSMENT & MEDALLION TRANSITION PLANNING

Assess the Data Store. Chart the transition. De-risk the move.

A data-driven assessment of the Skyworks Operational Data Store and a prioritized roadmap toward a Bronze / Silver / Gold medallion architecture, delivered through Findability Sciences' **I-CUPP** framework and the proprietary **Business Process Co-Pilot**.

ENGAGEMENT

16 weeks · fixed scope

FRAMEWORK

I-CUPP · BPC-enabled

DELIVERABLES

9 · Skyworks-owned

THE I-CUPP FRAMEWORK

I**Infrastructure**

SKYWORKS

C

Collection

U

Unification

P**Processing**

BPC

P

Presentation

— THE ENGAGEMENT

A fixed-scope assessment that hands Skyworks a validated transition strategy.

Skyworks' ODS today serves double duty as both a transactional and an analytical layer. We assess the current state, establish metadata and lineage visibility, and produce a recommendation engine that classifies datasets, models cost and performance, and prioritizes the migration, without touching production.

DURATION

16 wks

12 active + 4 acceptance

FRAMEWORK LAYERS

5

I-CUPP, end to end

PHASES

4

Discovery → handover

DELIVERABLES

9

All Skyworks-owned

FS TEAM

5

Dedicated personnel

◆ WHAT YOU WALK AWAY OWNING

- Complete ODS metadata catalog
- Bronze / Silver / Gold classification
- Prioritized, low-risk transition backlog
- End-to-end lineage visibility
- Calibrated cost & performance model
- Execution playbook + executive package

ENGAGEMENT POSTURE

Read-only, advisory, non-disruptive. We recommend; Skyworks retains full decision authority over what to act on and when.

— CURRENT STATE

One Data Store, two jobs, and the cost shows up at peak.

The ODS carries both transactional processing and analytical reporting on the same footprint. That overlap is where performance ceilings, governance blind spots, and compute inefficiency originate.

ODS SIZE

1.7 TB

COMPUTE

22 CPUs

ACTIVE SSIS JOBS

~250

PEAK CONCURRENCY

1,231 batch/s

PERFORMANCE

Transactional and analytical workloads contend for the same resources, constraining throughput at peak batch concurrency.

GOVERNANCE

Limited lineage and metadata visibility makes ownership, dependencies, and downstream impact hard to see.


COST

A single tier doing both jobs leaves compute spend poorly matched to the value each dataset actually delivers.

The medallion target: **Bronze** (raw), **Silver** (conformed), and **Gold** (curated) separate these concerns. This engagement decides *what moves where*, in what order, and at what impact.

— HOW WE RUN THE ASSESSMENT

Five layers. Infrastructure is yours; the four above are ours.

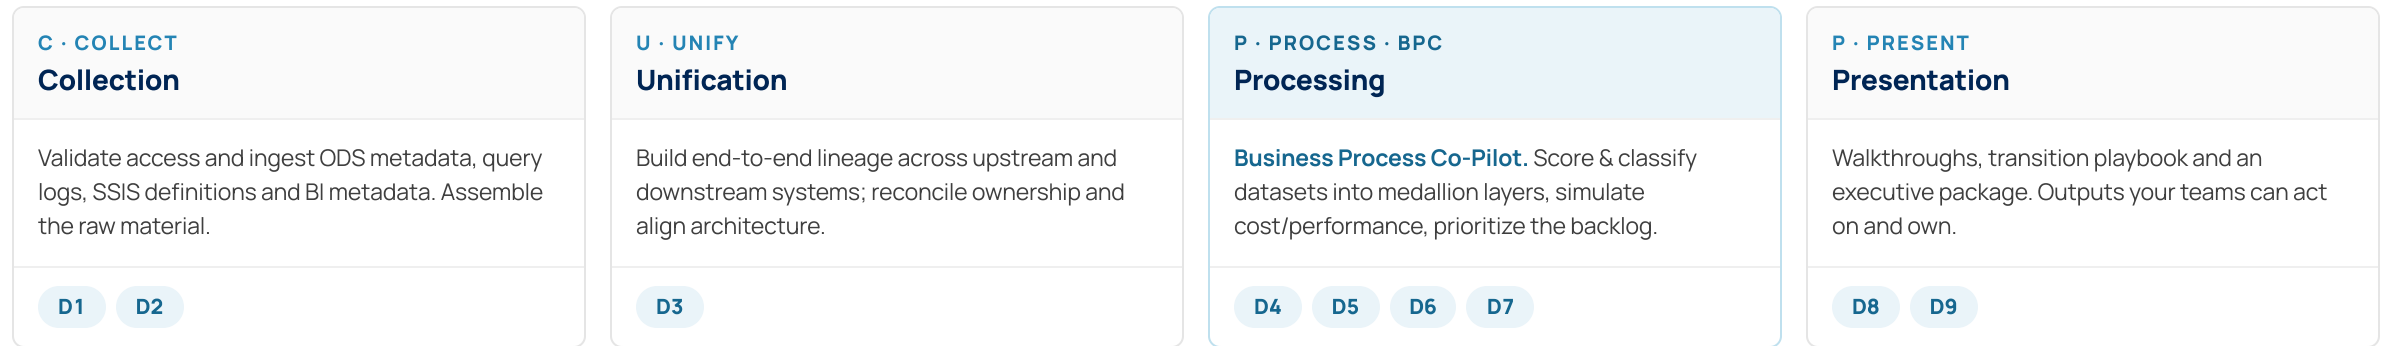

I **Infrastructure, owned by Skyworks**
The existing ODS estate and platform decisions sit here. We assess on top of it; we do not provision, license, or deploy it. Your input defines this layer.

SKYWORKS INPUT

Collection → Unification → Processing → Presentation is the data flow. Every deliverable maps to exactly one layer · see slide 10.

Your platform, your call. We assess on top of it.

Findability Sciences does not provision, license, or stand up infrastructure. The assessment runs against the environment Skyworks already operates. This layer is defined and confirmed by Skyworks.

CURRENT ODS · CONFIRMED

SIZE

1.7 TB

COMPUTE

22 CPUs

SSIS JOBS

~250

PEAK

1,231 b/s

◆ TO CONFIRM OR SELECT · SKYWORKS INPUT

TARGET PLATFORM

Select... ▼

ACCESS MODEL

Select... ▼

ENVIRONMENT / INSTANCE

e.g. ODS-PROD region / host

ACCESS GRANTOR / DATA OWNER

Name, role / team

READ-ONLY ACCESS GRANTED BY

dd mmm yyyy

CAPTURED BY

Your name

LINEAGE REFERENCE SYSTEMS AVAILABLE VIA API

☐ SAP ERP☐ Kinaxis☐ SKY Apps☐ PLM☐ EDI☐ PROMIS☐ CRM☐ Warehouse☐ Enterprise Analytics

Save inputs

Export JSON

Clear

Fabric provisioning, environment setup, licensing and infrastructure deployment are **out of scope** (see slide 12). Lineage coverage is subject to the API and metadata availability you confirm above.



— C · COLLECTION

Assemble the raw material: metadata, logs, pipelines.

Connect to the ODS and capture everything the later layers depend on. Read-only, automated where possible, and surfaced as a clean inventory.

ACTIVITIES · WEEKS 1-3

- 01 **Connectivity validation:** confirm ODS access and identify any constraints.
- 02 **Automated metadata ingestion:** tables, schemas, columns, sizes.
- 03 **Query-log analysis:** usage patterns, frequency, access tools.
- 04 **SSIS package parsing:** map transformation logic flowing through the ODS.
- 05 **BI / reporting metadata** capture for reports drawn from the ODS, where available.
- 06 **Data ownership identification** + lineage reference system availability check.

D1 CONNECTIVITY STATUS REPORT

Access validation for ODS metadata and lineage reference systems, with any limitations flagged.

D2 ODS METADATA INVENTORY

Complete catalog of datasets, tables, schemas, columns, SSIS definitions and associated metadata.

CUPP PARALLEL


The Collect stage: internal data gathered before judgment is applied.

— U · UNIFICATION



Make it coherent: lineage across the whole estate.

Trace each ODS dataset from where it originates to where it is consumed. Reference systems give context for lineage only, with no deep ingestion of them.

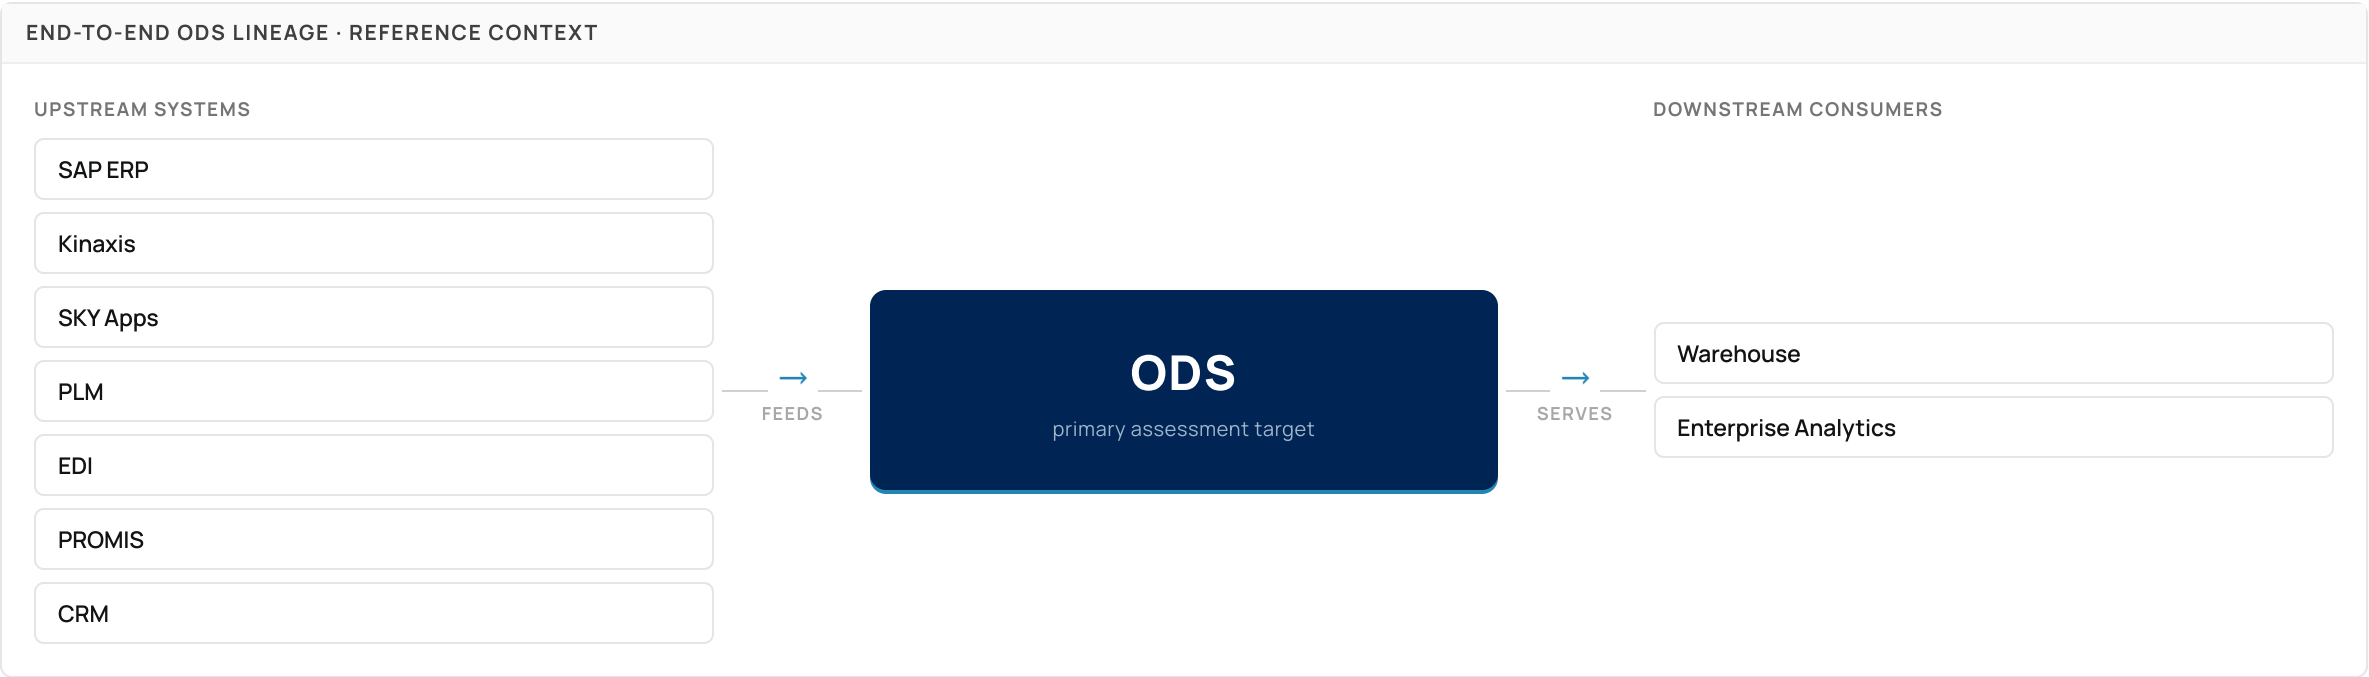

ACTIVITIES · WEEKS 4-7

- Upstream system tracing
- Data ownership mapping
- Downstream dependency identification
- End-to-end lineage visualization

D3 END-TO-END ODS LINEAGE MAP

Feeds the [Architecture Alignment Baseline \(D5\)](#) built in Processing.



— P · PROCESSING · BUSINESS PROCESS CO-PILOT


The BPC engine classifies, simulates, and prioritizes.

Our proprietary accelerator turns the inventory and lineage into decisions: which dataset belongs in which medallion layer, what each move costs and saves, and what to do first.

BPC ENGINE · WEEKS 4-10



CLASSIFICATION OUTPUT



DELIVERABLES



Recommendations are **advisory**. Skyworks retains full decision authority over which datasets to act on and the timing.



— P · PRESENTATION

Outputs your teams can act on and own.

A model and a playbook are only useful if the people executing trust them. The final layer turns analysis into enablement: walkthroughs, guidance, and a leadership decision package.

ACTIVITIES · WEEKS 11-12

- 01 **Deliverable walkthroughs** with the execution teams.
- 02 **Transition playbook:** step-by-step, incremental, team-led execution.
- 03 **Executive recommendations** and business-case summary.
- 04 **Knowledge transfer & handover** sessions with stakeholders.

D8 TRANSITION PLAYBOOK

Step-by-step guidance for Skyworks teams to execute prioritized transitions incrementally.

D9 EXECUTIVE SUMMARY REPORT

Findings, recommendations and business case for leadership review.

YOURS TO KEEP

All deliverables ship as exportable documents, data files and interactive models, owned by Skyworks on payment.

— DELIVERABLES


Nine deliverables, each owned by one layer.

#	DELIVERABLE	I-CUPP LAYER	PHASE	WEEKS	PURPOSE
1	Connectivity Status Report	Collection	Ph 1	W1-3	Validate ODS access; identify constraints
2	ODS Metadata Inventory	Collection	Ph 1	W1-3	Centralized metadata catalog
3	End-to-End ODS Lineage Map	Unification	Ph 2	W4-7	Data-flow visibility, origin to consumer
4	ODS Dataset Classification Report	Processing · BPC	Ph 2	W4-7	Bronze / Silver / Gold recommendations
5	Architecture Alignment Baseline	Processing · BPC	Ph 2	W4-7	Current-state gap analysis
6	Cost & Performance Simulation Model	Processing · BPC	Ph 3	W8-10	Migration impact, calibrated to Skyworks
7	Prioritized Transition Backlog	Processing · BPC	Ph 3	W8-10	Ranked migration opportunities
8	Transition Playbook	Presentation	Ph 4	W11-12	Execution guidance for your teams
9	Executive Summary Report	Presentation	Ph 4	W11-12	Leadership decision package

Infrastructure (Layer I) carries no FS deliverable by design. It is the Skyworks-owned foundation the other four layers operate on.

— TIMELINE

Twelve weeks active, four for acceptance.

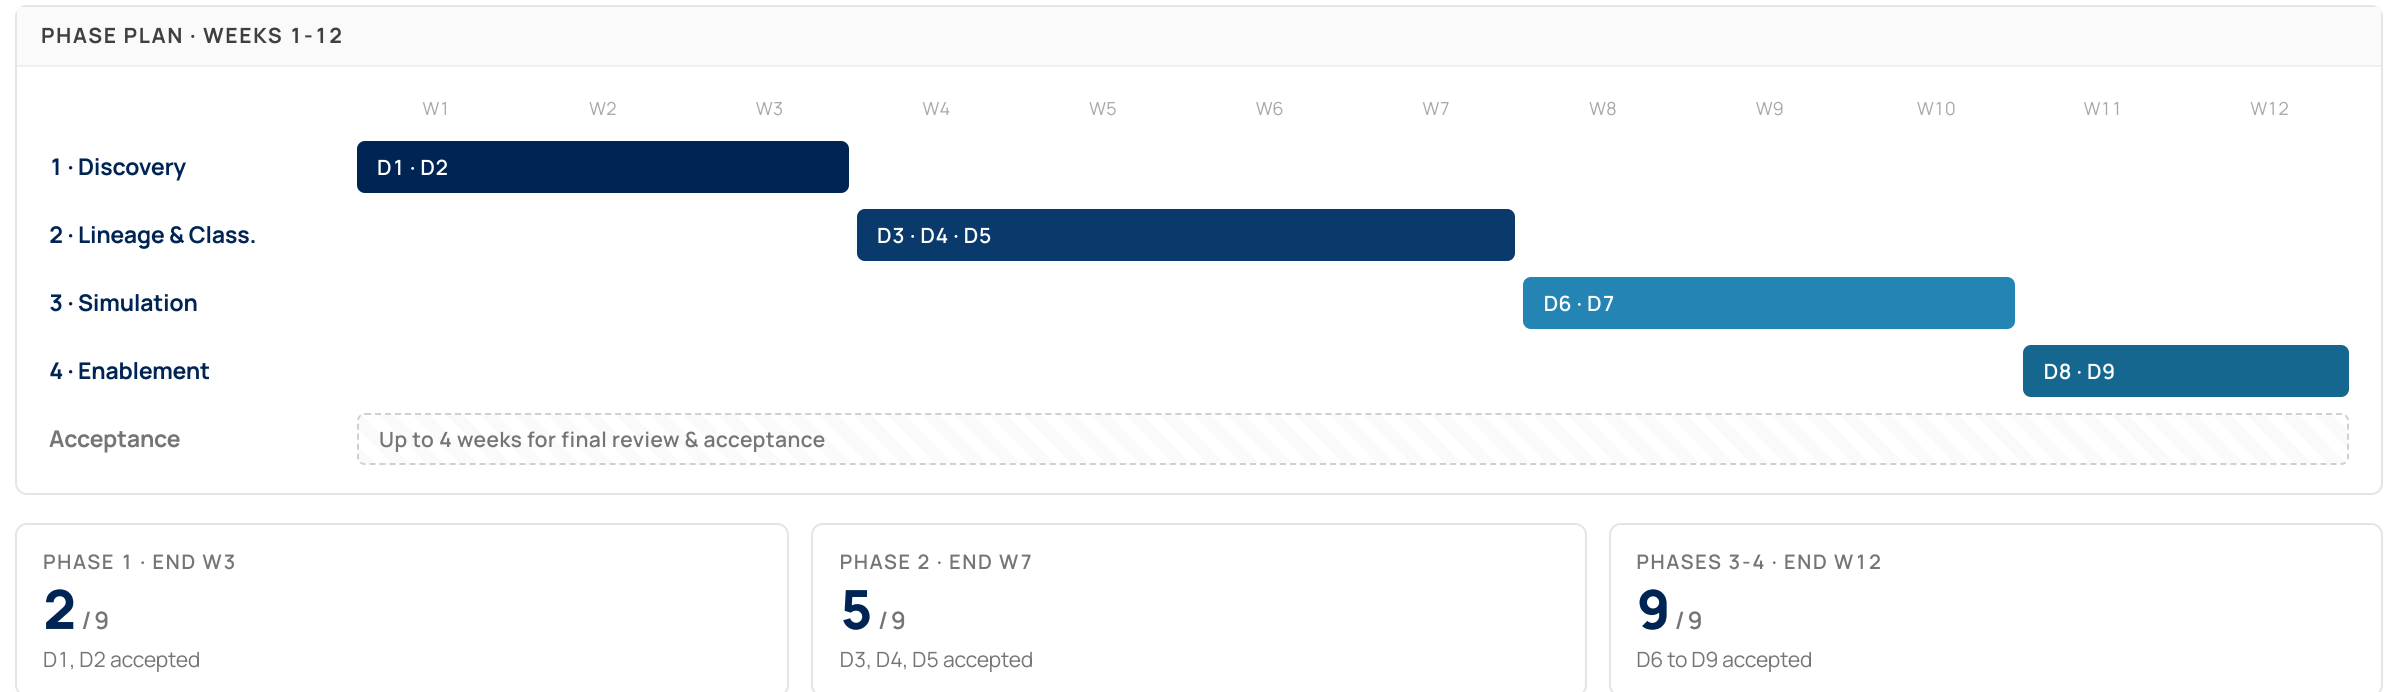

Deliverables are accepted cumulatively against a **10 business-day** review window each. The 12-week plan assumes read-only access within 5 business days of SOW execution; access delays extend the timeline proportionally.

— BOUNDARIES

What this engagement does not do.

Clear edges keep the assessment fast and low-risk. The items below are explicitly excluded, and handled by Skyworks or a designated partner, or scoped separately via change request.

Platform & Infrastructure

EXCLUDED

- × Fabric provisioning
- × Environment setup
- × Licensing activities
- × Infrastructure deployment

Migration Execution

EXCLUDED

- × Physical migration of datasets
- × Moving data into Bronze/Silver/Gold
- × Production cutovers
- × Execution activities

Development

EXCLUDED

- × Modifying SSIS packages
- × ETL redesign / redevelopment
- × New pipeline development
- × BI report build or redesign

Data Remediation

EXCLUDED

- × Data quality fixes
- × Data cleansing
- × Master data remediation
- × *We surface issues; Skyworks resolves*

Operations & Support

EXCLUDED

- × Ongoing monitoring
- × Long-term administration
- × Post-engagement support
- × Platform access beyond term

Broader Systems

EXCLUDED

- × Deep ingestion of non-ODS systems
- × Independent upstream/downstream assessment
- × Reference systems = lineage context only

— TO START STRONG

What we need from Skyworks.

A focused set of inputs keeps the 12-week plan on track. The access SLA is the single biggest driver of timeline.

RESPONSIBILITIES	
01	Designate a project sponsor and a day-to-day technical point of contact .
02	Provide read-only access to ODS databases, query logs, SSIS repositories and BI tools.
03	Make SMEs available for weekly 1-hour working sessions.
04	Supply business domain context and data-ownership information.
05	Participate in weekly status reviews and milestone sign-off gates.

ACCESS SLA

5 business days

From SOW execution, read-only

KEY ASSUMPTION

The timeline assumes ODS access within 5 business days. Delays extend the schedule proportionally. No write access to production is required at any point.

— AT HANDOVER

From assessment to a confident first move.

◆ YOU WILL HAVE

- ✓ A validated migration strategy
- ✓ A calibrated cost & performance model
- ✓ Full lineage & metadata visibility
- ✓ A prioritized, low-risk roadmap
- ✓ Implementation guidance (playbook)
- ✓ An executive decision package

NEXT STEPS

- 01 Confirm sponsor + technical POC.
- 02 Complete the Infrastructure inputs (slide 5).
- 03 Provision read-only access, within 5 days.
- 04 Schedule the Phase 1 working session.

PREPARED FOR



DELIVERED BY



Let's begin.

Kick-off · ODS Assessment & Medallion Transition Planning

